

2023 INSPECTION & TEST PLAN

STATIC DATA								
Plant	Manitou	Eq#	66155552	Manufacturer	Wilco Industries			
LSD	01-30-044-26W3	Tag #	T-103	Serial #	016349-04			

Summary

Due	Method	Completed by	Certification
2023	Visual internal (VI)	API 653 Certified AGST Inspector	API 653
2023	Visual external (VE)	API 653 Certified AGST Inspector	API 653
2023	Ultrasonic testing (UT)	NDE contractor – UT technician	CGSB level 1 or 2
2023	Magnetic Flux Leakage (MFL)	NDE contractor – MFL technician	As Per API 653 Annex G

Preparation

- o Ensure safe access to all areas of the tank internal and external.
- o Tank to be internally clean and dry on floor, first course and up the 2nd shell as high as possible.
- o Ensure all nozzles and couplings are cleaned out and dry for visual inspection.

Notes

Inspection to be done in accordance with attached HUSKY TASKLIST QNATANK-2

VI & VE

Notes

Visual inspection to be completed by API 653 Above ground storage tank inspector

MFL &UT

Notes

- MFL examination of the floor to be completed by qualified technician as per API 653 Annex G
- MFL indications to be examined with UT and measurements to be mapped
- UT on Tank shell to be completed every 2' around the circumference, from 6" elevation to the top leg of the floor to shell weld.
- Add measurements and locations to CML Map.
- CML's must be scanned, and the minimum thickness is to be recorded
- If corrosion is found, technician must comment on the nature of the corrosion (e.g., localized corrosion, pitting, etc.)
- Any questions regarding the scope of examination please call Terry Neufeld 780-818-8468

Area	Thickness	Action Required		
Nominal Thickness	Floor: 0.250"; Shell: 0.250" Roof: 0.188"	None		
Minimum Required	Floor: 0.100" (API 653 Table 4.4)			
Thickness	Shell: 0.100"	UT - flag RED		
Alert Thickness	Floor: 0.140"	UT - flag YELLOW		



QNATANK-2 5Y Code Inspection Tank 400 to 1000 bbl, Uncoated

This task list is not all inclusive and does not limit any additional inspection or examination or limit the areas to be examined. The inspector may use any additional reasonable means deemed necessary to determine the integrity of the tank for code compliance and suitability for continued service

External Inspection

All deficiencies are to be recorded and photographs taken All evidence of corrosion is to be mapped and depth measured with pit or depth gauge

Ladders, stairways and platforms

- 1) Handrails, inspect for pitting, holes and paint condition condition of attachment welds condition of mid rails and toe boards condition of safety drop bars for corrosion, operation, and length
- 2) Platform frame inspect for corrosion and paint failure corrosion and cracking of attachment welds reinforcing pads where supports are attached to the shell and roof thinning and holes in the deck plate or distortion of the grating seal welds on flat-surface to flat-surface junctures
- 3) Deck plate and grating, inspect for corrosion, holes and paint failure scale build-up on plate to frame weld thinning of bars and failure of welds on grating

All deficiencies to be noted. Unsafe conditions to be brought to the attention of Operations for immediate repair.

Unsafe items are not to be used during inspection.

Foundation and site



- 1) Foundation inspect for measure foundation levelness and bottom elevations. type of foundation cavities under foundation and vegetation against bottom of the tank. verify that runoff rainwater drains away from the tank settlement around perimeter of tank. areas where leaching of oil has left rock filler exposed
- 2) Site and dike inspect for condition of the dike drainage away from the tank and associated piping and manifolds operation of dike drains buildup of trash, vegetation, and other inflammables.

Shell and appurtenances

- 1) Shells inspect for paint failures, pitting, and corrosion corrosion and thinning at the bottom angle area where the floor and shell are attached dents, bulges or buckling
- 2) Manways and nozzles, inspect for cracks or signs of leakage on the weld joints at nozzles, manway, reinforcing plates shell dimpling around nozzles flange leaks around manways and nozzles, sealing of insulation around manway flange and nozzles. Inadequate manway flange and cover thickness on mixer manways
- 3) Tank piping manifolds, inspect for leak around valves, piping and flanges fire fighting system components anchored piping that could damage the tank shell or bottom connections during earth movements adequate thermal pressure relief of piping to the tank operation of regulators for tanks with purge gas systems leaks around sample connections damage and check accuracy of temperature indicators



If deficiencies are noted additional inspection of associated piping or support system is required to determine cause and recommended resolution

4) Autogauge system, inspect for leaks around the tape guide and lower sheave housing damage to autogauge head proper movement of the tape condition of the board and legibility of board type autogauges freedom of movement of the marker and float

All deficiencies to be noted and brought to the attention of Operations for immediate repair.

- 5) Shell mounted sample station inspect for function of valves and plugged lines including drain line and return to tank line leaks around circulation pump and operating problems damaged bracing or supports for sampling system and piping
- 6) Heater, inspect for presence of product in condensate drain line from steam type heater leaks around bolting flange for heater inlets
- 7) Overflow lines inspect for screens are clean corrosion no plugs in lines broken connections freeze damage
- 8) Shell insulation, inspect for cracks or leaks in the insulation weather coat wet insulation under the weather coat corrosion under insulation by removing sample areas

Roof and appurtenances

NOTE: For safety, before accessing the roof, check with an ultrasonic instrument near the edge of the roof for thinning. Verify the roof thickness is sufficient for safe support. (Corrosion normally attacks the deck plate at the edge of a fixed roof and at the rafters in the center of the roof first)



- 1) Deck plate inspect for, paint failure, pitting, holes and corrosion product on the roof deck
- 2) Deck drainage, inspect for indications of standing water
- 3) Roof insulation, inspect for cracks or leaks in the insulation weather coat wet insulation under the weather coat corrosion under insulation by removing sample areas
- 4) Sample hatch inspect for condition and functioning of the sample hatch cover condition of the seal inside of the hatch cover corrosion and plugging on thief and gauge hatch cover marked and tab stating hold off distance (where sample hatch is used to gauge product level condition of any internal lining of the sample hatch
- 5) Gaugewell inspect for thinning of the visible portion of the well, size of slots and cover condition hold off marker and tab for legibility condition of roof guide and rollers on gauge well for floating roofs distance from gauge well to tank shell at different levels if accessible
- 6) Pressure / Vacuum breakers, inspect for proper operation, size, number, and type
- All deficiencies to be noted and brought to the attention of Operations for immediate repair.

External NDE

- 1) Complete ultrasonic thickness survey in accordance with tank UT circuit drawing
- 2) Perform additional ultrasonic, liquid penetrant or magnetic particle inspection necessary to verify tank condition and integrity at identified areas of mechanical damage, blistering, cracks or corrosion.



Internal Inspection

All deficiencies are to be recorded and photographs taken All evidence of corrosion is to be mapped and depth measured with pit or depth gauge

General

- 1) Ensure tank has been high pressure washed or steamed to remove residual product to Class 3 cleanliness.
- 2) Shell inspect for banding and peaking of shell welds corrosion of the shell roundness and out of plumb corrosion at the critical zone of the floor to shell joint
- 3) Floor inspect for corrosion of floor underside voids under the bottom indications of leakage floor to shell edge settlement
- 4) Roof inspect for corrosion, holes and other deterioration broken welds in shell to roof joint
- 5) Internal heaters inspect for broken or damaged piping debris accumulation corrosion of components coating damage from overheating accelerated corrosion of the floor and shell in the area of the heater
- 6) Piping and sumps inspect for corrosion and coating condition pluggage holes distortion at shell to pipe connection

INTERNAL NDE

1) Perform ultrasonic thickness checks of internal nozzle projections, coils and permanent internals exhibiting corrosion and metal loss.



- 2) Perform additional NDE per vessel's last inspection report recommendations
- 3) Perform additional ultrasonic, liquid penetrant or magnetic particle inspection necessary to verify vessel condition and integrity at identified areas of mechanical damage, blistering, cracks or corrosion.

Husky Energy

Tank Inspection Report


Location: 01-30-0	144-26W3	Tank Type:	-103 Slop tarl	Date: Oct 19 2018
Mfg: Wilco IND.	Year bl	t: 2008	S/N:016349-04	CAP: 1000 bbl
Floor Thk: 1/4"	Shell Thk: <u>14</u>	" 3/16"	Roof Thk: 3/16	
Requisitioned by: Kyle	Forbes	Approver: Kyle	Forbes Ap	prover Code: 22- 02017604
wo#: 81291186	PO#: 8401228100	cc:	SAP #: 66	155552

	: <u>81291186</u> po#:_8	10.0	2810	_	_ 0
EXTE	RNAL INSPECTION:				
		Τ,,			See
ID	Item	Yes	Good	N/A	Notes
	GENERAL				
T1	Other (Please Explain)				
T2	Corrosion			V	
T3	Leaks			V	
T4	Vibration			V	
T5	Dissimilar Flange Rating			V	
T6	Ladder/Stairway	V	/		
T7	Platform	~	1		
T8	Electrical Ground	V	/		
T9	Cathodic Protection			V	
T10	Painted Inactive Corrosion			V	
T11	Coating/Painting			V	
T12	Level Gauge	IV.	V		
T13	Bottom	V	V	/	
T14	Secondary Containment		/	V	
T15	Shell	V	V.		
T16	Roof	1	/		
T17	Agitator/ Mixer			V	l .
	SUPPORTS				
T31	Other (Please Explain)				
T32	Foundation	1	V	/	1
T33	Anchor Bolts			V	
T34	Windgirders			V	
	CONNECTIONS				
T41	Other (Please explain)				
T42	Small Branches	1/	1	-	
T43	Nozzles	V	V	-	
T44	Pipe Manifolds			V	
T45	Swing Lines			V	
T46	Manways/Hatches	V	V		
T47	Reinforcing Pads	V	V		
T48	Inadequate Thread Engagement		-	V	
T49	Bolting		V		
T50	Flanges				
T51	Leak Clamps			\checkmark	
	INSULATION				
T61	Other (Please explain)				
T62	Damage			V	
T63	Penetrations	1	/		
T64	Jacket			1	
T65	Banding			V	
T66	Seals/Joints	1		1	
	RELIEF DEVICE				
T7t	Other (Please explain)	1			_
T72	Corrosion	1-			
T73	Leaks				
T74	Restricted InleUOutlet			-	
1/4					

INTERNAL INSPECTION:

ID	Item	Yes	Good	N/A	See Notes
	GENERAL				
T1	Other (Please Explain)				
T2	Corrosion			V	
T3	Erosion			V	
T4	Distortion			V	
T5	Blisters			V	
T6	Deposits		,	V	
T7	Welds	1	1		
T8	Nozzles	V	V.		
T9	Shell	V	/		
T10	Roof	1	/		
T11	Floor	V	V		
	GENERAL		1		
T21	Other - Firetube		/		2
T21	Other - Anodes			V	
T22	Annular Ring			V	
T23	Sump			V	
T24	Roof Supports			V	
T25	Thermowells	1	V		
T26	Metallic Linings			V	
T27	Non Metallic Linings				
T28	Internal Steam Coil / other Piping	1	V		
T29	Level Gauge	1	1/		3
T30	Other Welded Attachements	/	V		
Bacl	welding Req'd			V	

ID	Notes
I	Tonk Set on ground
2	Firetibe appears to be straight
3	Recommend removing the float guide wires
	90.00 001115
_	
_	
_	

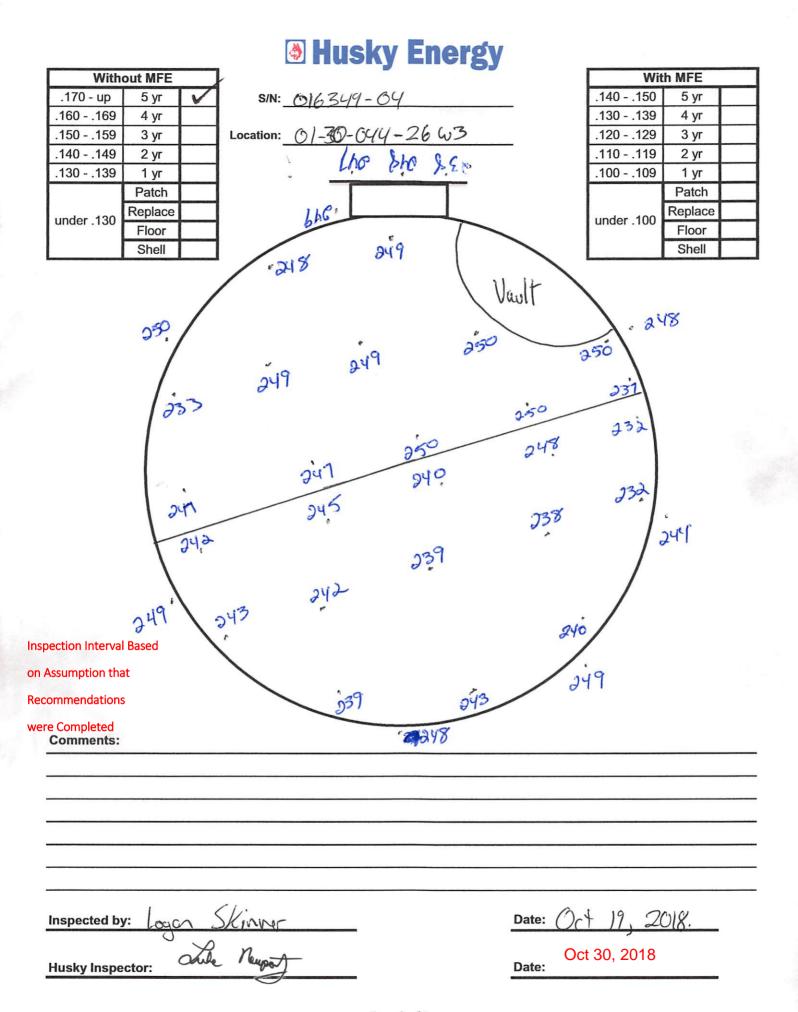



NONDESTRUCTIVE INSPECTION REPORT

CA1213-NDT-23

Page 1 of 1

Type of Inspection: VT/ UT

Rev: 3.0

Test Technique: UT thickness

Equipment: DMSGO, FH2E, Flashlight, Grinder

Code/Standard: Client Information

Client: HUSKY OIL OPERATIONS LIMITED

IRISNDT #: LYN1801663 Location: 01-30-044-26W3

Item Inspected: Tank T-103 SN: 016349-04

Date: 19-Oct-18 WO #: 81291186 PO #: 8401228100

Appr# 2Z-02017604

A UT and Visual inspection was carried out on the following 10000BBL oil tank for the purpose of continued fitness for service and determination of inspection interval. See the field report for results of inspection, UT recorded values and inspection interval.



Recommendations:

-Recommend removing the float guide wires

Tank suitable for service

Inapportion Limitation(a)

Note: Spot UT carried out on the floor and shell as a representation of overall integrity not a 100% scan method. DMSGO # 31139 cal. date due. June 1 2019 Probe: FH2E SN: SCA0620

Only 1st source slagged for inspection

inspection Lim	itation(s). Only	isi course c	cleaned for inspection		
Unit#: 667	Kilometers: Out: Hrs: Out: Hrs:		Consumables: Min Requested By: Kyle Forbes Approver: Kyle Forbes	Interpretation by: Logan Skinner (Print) (Sign)	SNT-TC-1A: UT-1 C.G.S.B.: 1 (Level) C.G.S.B#: 17159
Personnel: Logan Skinner				Client Representative: (Print) Karen Ha lam in full agreement with report contents (Sign)	awryluk

5311 - 86 Street NW, Edmonton, Alberta T6E 5T8 Phone (780) 437-4747 Fax (780) 436-4873 Calgary (403) 279-6121 Cold Lake

Lloydminster (780) 875-6455 Barrhead (780) 674-3018 Nisku (780) 955-7616 Cold Lake Fort McMurray Red Deer (780) 826-6105 (780) 743-1536 (403) 347-1742 Engineering, Calgary (403 Engineering, Edmonton (780 Rope Access Services (780 Offices also located in USA and UK

(403) 217-9684 (780) 437-2022 (780) 437-2022



DAILY LEM TIME-TICKET

IRISNDT DAILY TICKET#

CA1213-DT-125
Page 1 of 1

Custom	er: HUSK	Y OIL OPERATIONS LIMITED	IRISNDT DISPATO	CH #:	LYN180	1663	Locat	ion: 1-30-44-2	26W3	Date: 19	-Oct-18
Technici	an 1 : <u>Loga</u>	n Skinner Position: Se	enior Tech Technic	ian 2: _			Position:	Primary Activity: Other			
Technician 3: Position: Technician 4: Position:											
Time Start	Time Finish	Activity	Report #s	LOC	Total Hours	Total KMs	Description	PO/Cost Code/AFE		Job #/Work Order #/Other	
07:00	09:00	VT - Visual Testing	NDT-23	4	2	70	UT / VIS Tank T-103	P.O.#:	P.O.#: 8401228100		81291186
09:00	11:00	VT - Visual Testing	NDT-24	4	2		UT / VIS Tank T-104	P.O.#:	8401228100	W.O.#:	81291186
11:00	13:00	VT - Visual Testing	NDT-25	4	2	70	UT / VIS Tank T-105	P.O.#:	8401228100	W.O.#:	81291186
			(Totals for this page only)	Totals:	6	140	Unit: 667				
		Work Location (LO	C) Legend: 1) Inside Fab.	Shop	2) Ya	rd/Lay	down Area 3) Piping/I	Modular Fab.	Area 4) Other		
J.H.A. Carri	ed Out & Doo	cumented: Yes No Safety C	Concerns: Yes No Safety	y Meeting	: Yes	⊠ No	Living Out Allowance:	N/A ☐ Full	Bkfst Lunch	Supper 0	T Meal Hotel
			Equipment, S	Supplie	s, Cons	umable	s, and Other Costs				
Min											
			Additional	Site, Da	ailv. and	other r	elevant iob notes				
Additional Site, Daily, and other relevant job notes Approver: Kyle Forbes 2Z-02017604											
		AN NAME: Logan Skir (Print) GNATURE: (Sign)	1.	19-Oct-1	18		CLIENT NAME: Karer (Print) (Sign)	n Hawryluk	Cli	ent Date:	
